
SENTIENTLOGICS
Cognitive Visual Human Neural Ai

Date: 18.06.2026
Ref. No. 988/DubaiPolice/26

1. Solution Architecture Overview


1.1 System Architecture

This diagram illustrates the high-level architecture of the **Dubai Police Agentic AI Media Operations Platform** hosted on **Microsoft Azure**. The solution enables communication teams to create, review, approve, adapt, monitor, and govern media content through four specialized AI agents-Media Release, Campaign Creative, Screen Adaptation, and Monitoring Intelligence-managed through a centralized Governance Dashboard.

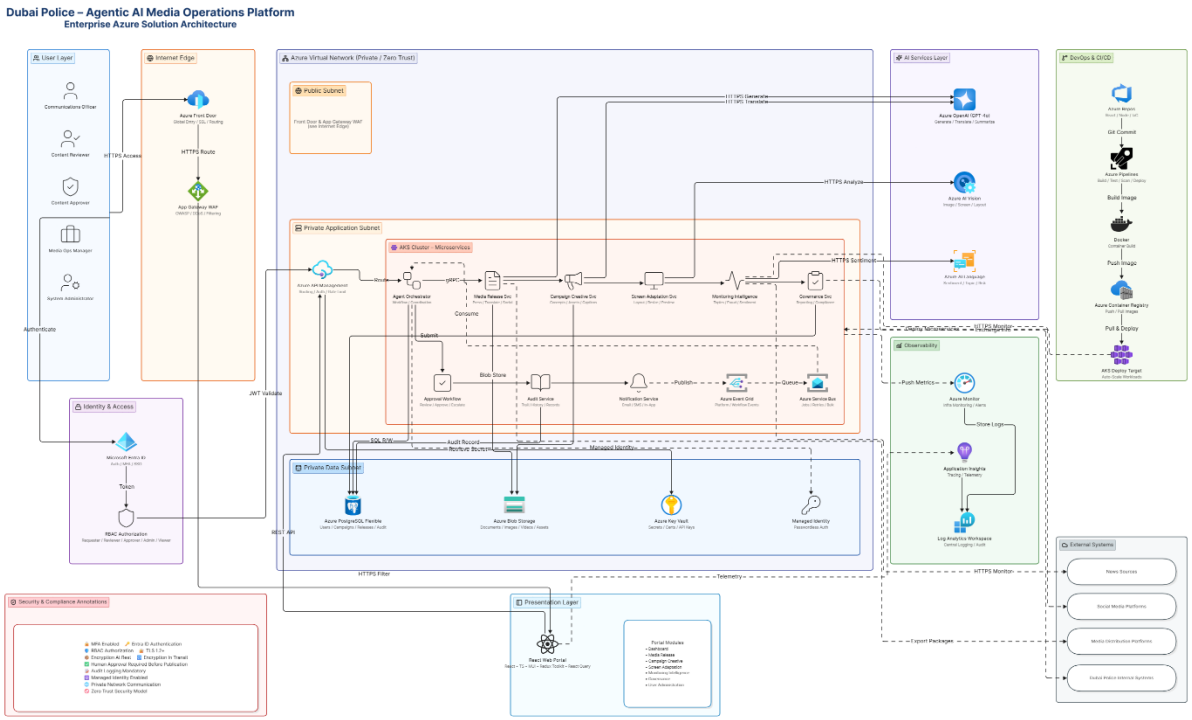


1.2 AI Model Selection, Routing & Governance Framework

This diagram illustrates how user requests are routed through an AI Gateway and classified to the appropriate AI agent-Media Release, Campaign Creative, Screen Adaptation, or Monitoring Intelligence. The platform enriches requests with prompts, context, and organizational knowledge, validates outputs through AI safety and governance controls, and ensures all content passes through mandatory human review and approval before publication. The entire process is monitored through audit logs, performance tracking, and observability mechanisms to maintain security, compliance, and accountability.

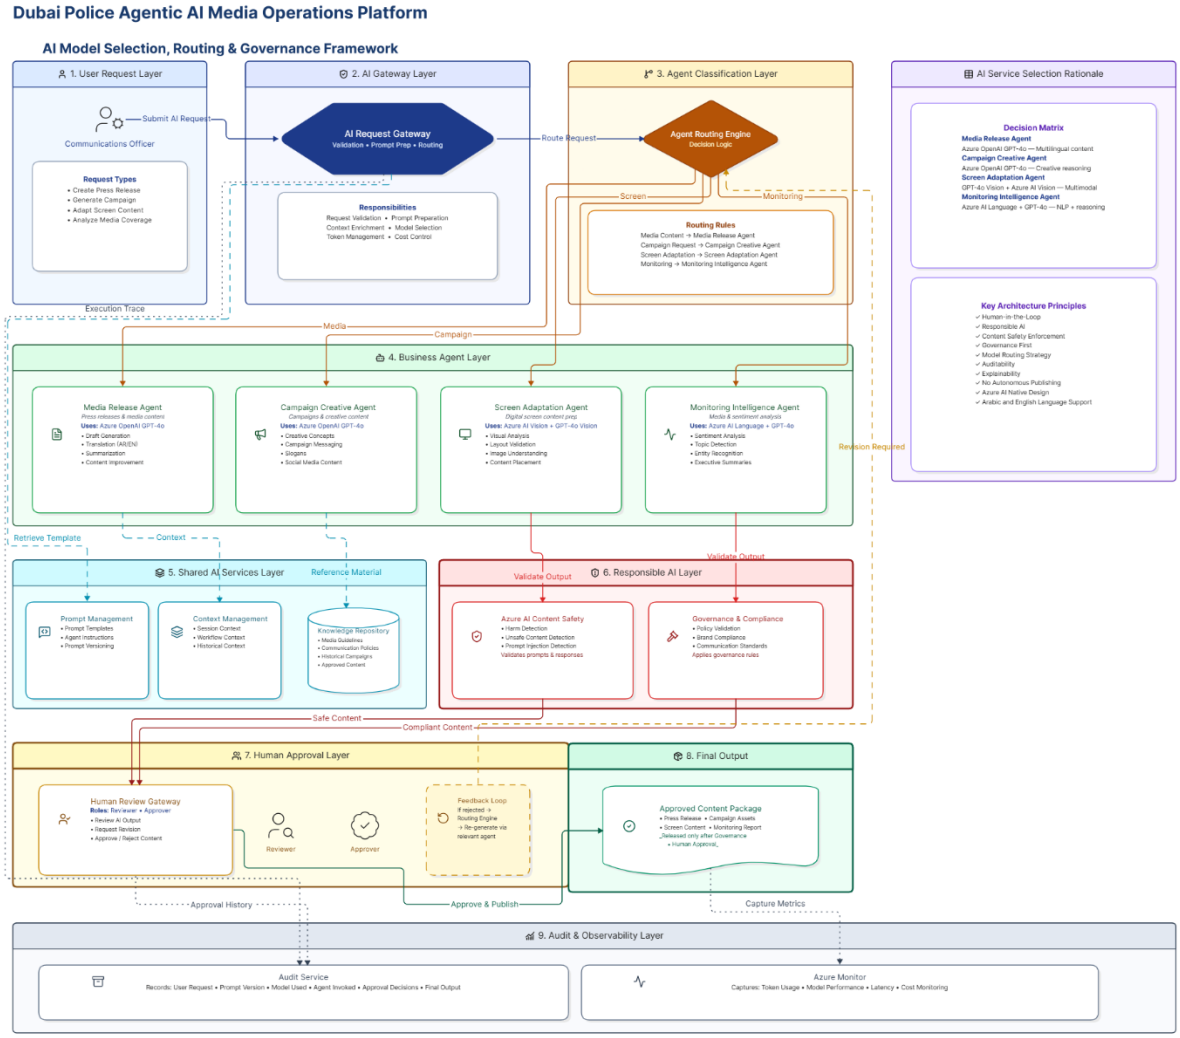

1.3 Multi-Agent Orchestration Framework Overview

This diagram illustrates the **multi-agent orchestration architecture** of the Dubai Police Agentic AI Media Operations Platform. A central **Supervisor Agent** receives user requests, determines the required workflow, and coordinates specialized agents for media release generation, campaign creation, screen adaptation, and monitoring intelligence. All agents share a common context and knowledge repository, while governance controls, compliance checks, audit logging, and mandatory human approvals ensure that every output is secure, compliant, and reviewed before publication.

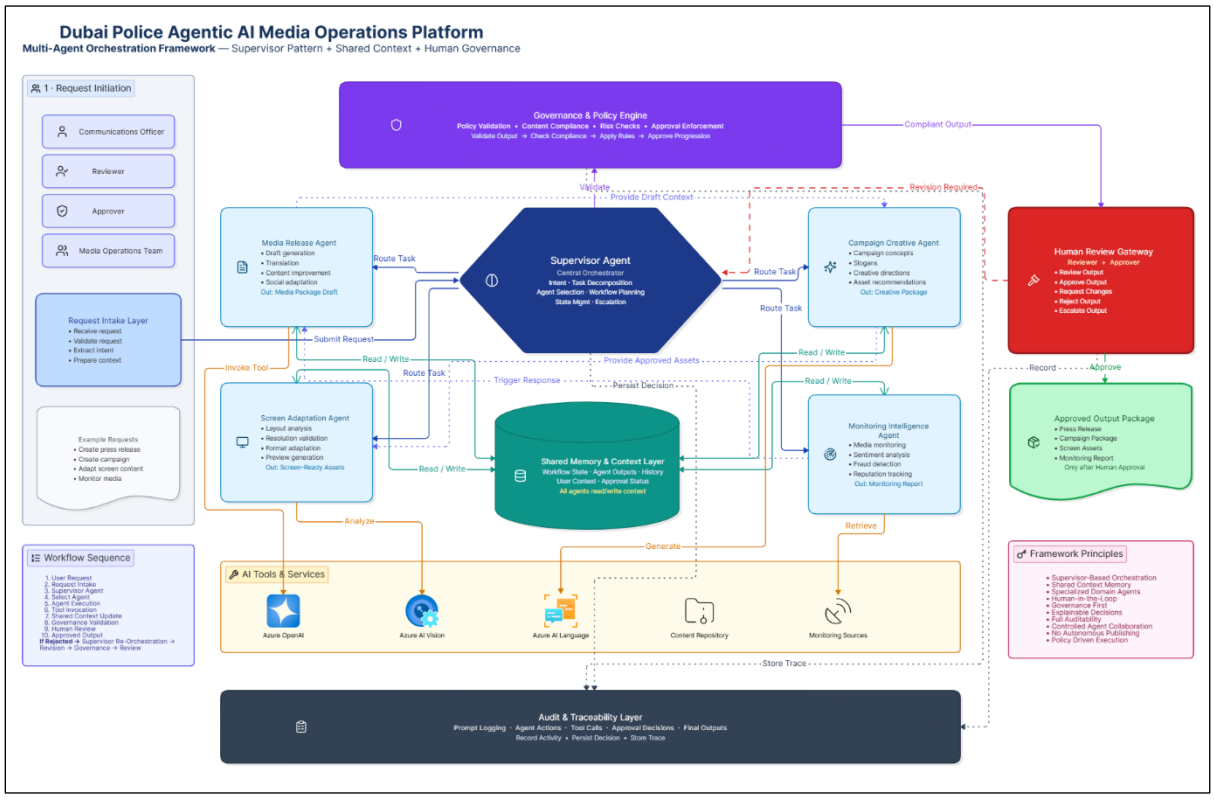


1.4 End-to-End Process Flow Overview

This diagram illustrates the complete workflow of the Dubai Police Agentic AI Media Operations Platform, from user request submission to final content delivery. User requests are processed by the appropriate AI agents for media release creation, campaign development, screen adaptation, or monitoring intelligence. All AI-generated outputs are routed through a mandatory human review and approval process, where content can be approved, revised, or rejected. Once approved, the content is packaged and distributed through the selected delivery channel, while all activities, decisions, and outputs are recorded in the governance and audit layer for compliance and traceability.

SENTIENTLOGICS

Cognitive Visual Human Neural Ai

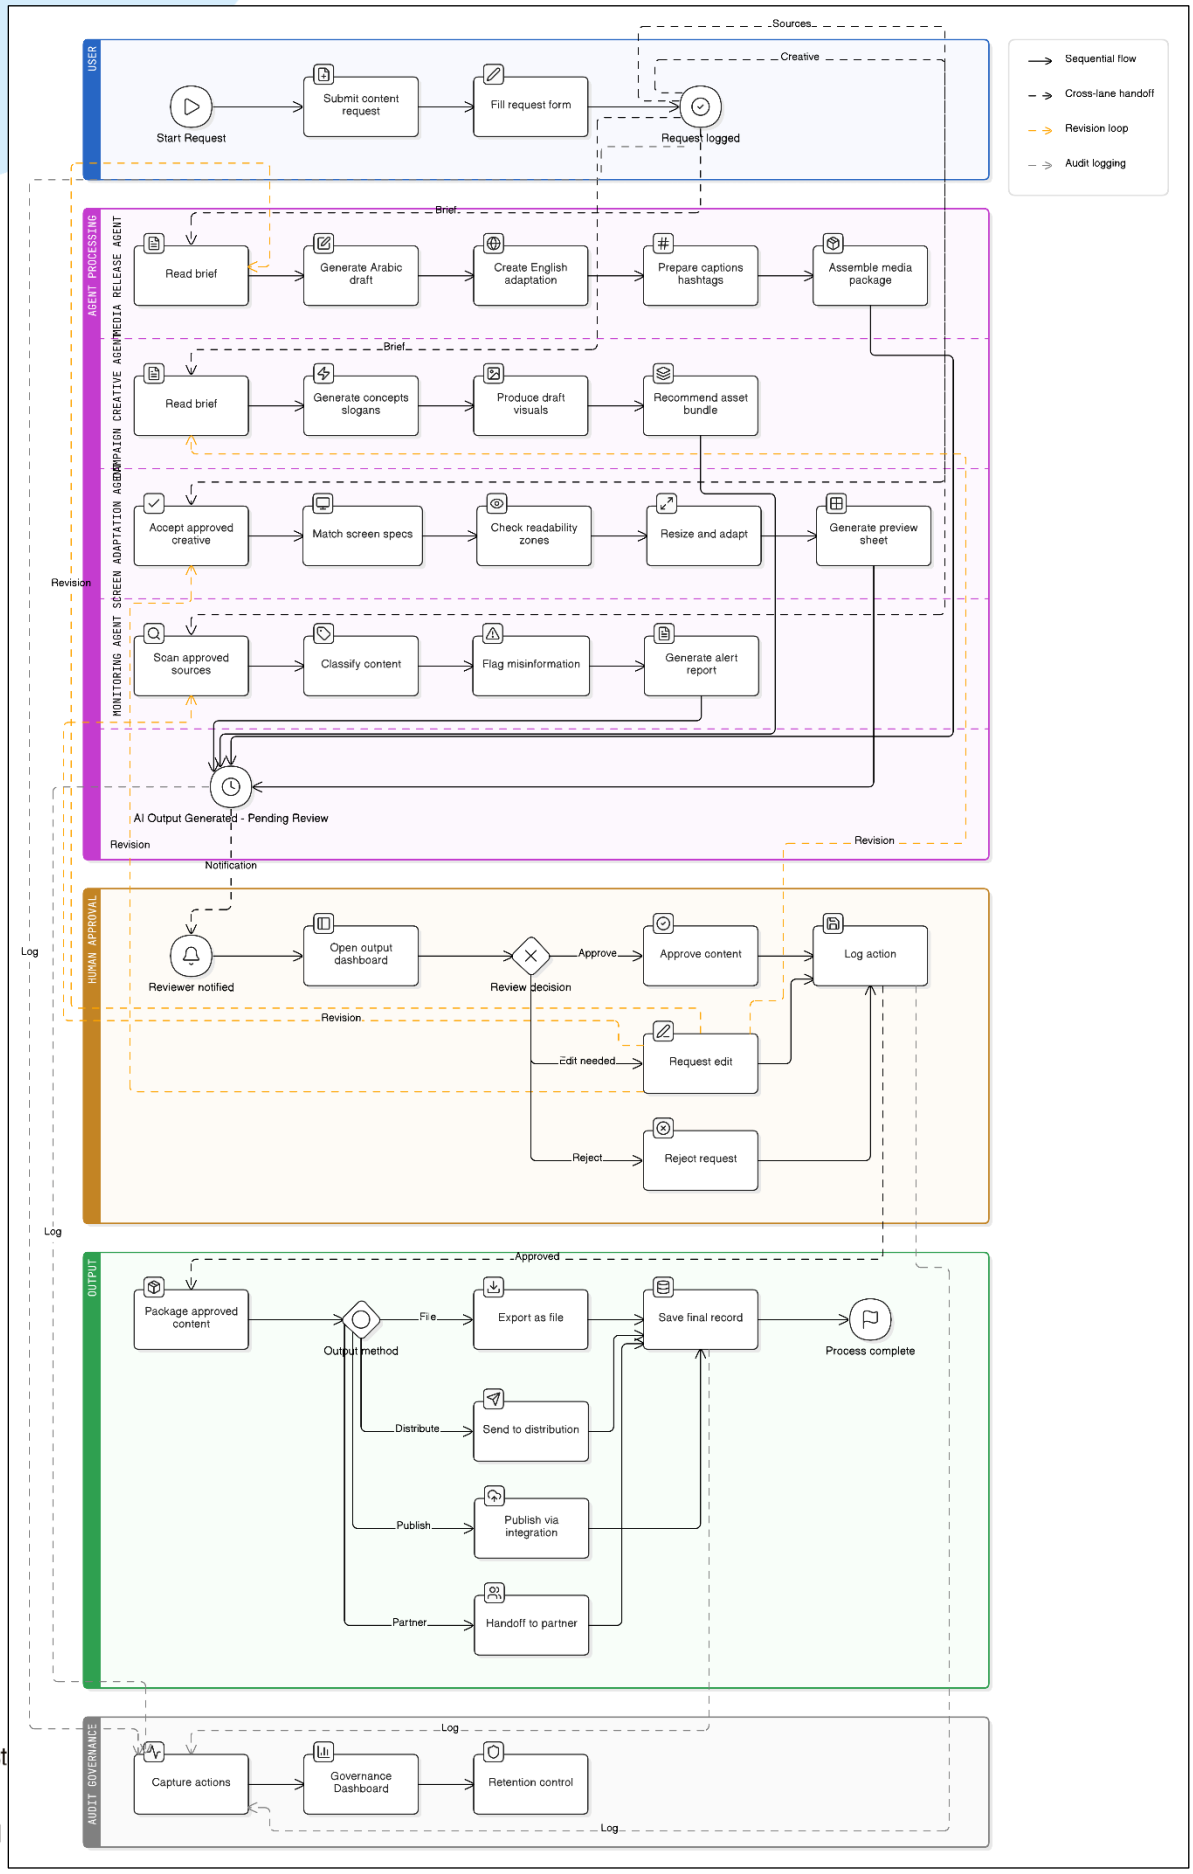

Regist

+971

2. AI Models, Hosting, Data Handling & Security

2.1 AI Models Strategy

The proposed solution utilizes Microsoft Azure AI services to provide secure, enterprise-grade AI capabilities while maintaining governance and human oversight.

Proposed AI Models

Capability	Proposed Service
Content Generation, Translation, Summarization	Azure OpenAI (GPT-4o)
Creative Campaign Generation	Azure OpenAI (GPT-4o)
Visual Content Analysis & Screen Adaptation	Azure AI Vision/GPT-4o Vision
Sentiment Analysis, Entity Recognition, Classification	Azure AI Language
Content Safety & Moderation	Azure AI Content Safety

Model Selection Rationale

- Strong Arabic and English language support.
- Multimodal capabilities (text + image understanding).
- Enterprise security and governance controls.
- Integration with Azure identity and monitoring services.
- Support for human-in-the-loop approval workflows.
- Ability to evolve toward private or government-hosted AI models in future phases.

2.2 Hosting Model Options

The solution is designed using containerized microservices and Kubernetes-based deployment patterns to support multiple hosting models.

Option A - Cloud Hosted (Recommended for Initial Deployment)

Platform

- Microsoft Azure
- Azure Kubernetes Service (AKS)
- Azure Database for PostgreSQL
- Azure Blob Storage
- Azure OpenAI

Benefits

- Faster implementation
- Elastic scalability
- Managed infrastructure

- Reduced operational overhead
- Native integration with Azure AI services

2.3 System Migration to Dubai Police Infrastructure

The proposed architecture is designed with portability as a core principle to support migration to Dubai Police-owned infrastructure as required by the RFQ.

Migration Readiness Strategy

Containerized Architecture

All application services are packaged as Docker containers and orchestrated through Kubernetes-compatible deployment models.

Infrastructure as Code

Environment provisioning can be maintained using Infrastructure as Code templates to enable repeatable deployment across environments.

Database Portability

PostgreSQL provides platform-independent deployment options and can be migrated between cloud and on-premise environments.

Storage Portability

Media assets and generated content are stored independently from application services, allowing migration without application redesign.

Deployment Portability

The solution is designed to support deployment on:

- Azure Kubernetes Service (AKS)
- Private Kubernetes clusters
- Government-managed container platforms

Migration Deliverables

The migration package may include:

- Source code repository
- Container images
- Infrastructure templates
- Deployment documentation
- Operations documentation
- Database migration scripts
- Knowledge transfer and handover support

2.4 Data Residency & Data Handling Approach

The solution follows a data minimization and controlled processing approach.

Data Processing Flow

Stage 1 - User Submission

Data entered through the application portal is received over encrypted HTTPS connections.

Stage 2 - Application Processing

Business workflows, approvals, and orchestration services process requests within the application environment.

Stage 3 - AI Processing

Only data required for AI processing is transmitted to approved AI services.

Examples:

- Press release content
- Campaign briefs
- Image assets
- Monitoring content

Stage 4 - Persistence

Approved content, workflow metadata, audit records, and user activity records are stored in controlled repositories.

Stage 5 - Publication

Only approved outputs are released through authorized publishing channels.

Data Storage Components

Data Type	Storage Location
User Profiles	PostgreSQL
Roles & Permissions	PostgreSQL
Workflow Status	PostgreSQL
Audit Metadata	PostgreSQL
Documents & Media Assets	Object Storage
Monitoring Results	PostgreSQL/Storage
System Logs	Centralized Logging Platform

2.5 Authentication, Authorization & Data Segregation

Authentication

The solution supports integration with enterprise identity providers.

Examples:

- Microsoft Entra ID
- Active Directory
- SAML 2.0
- OpenID Connect

Security Controls

- Single Sign-On (SSO)
- Multi-Factor Authentication (MFA)
- Centralized identity management
- Password policy enforcement

Role-Based Access Control (RBAC)

Illustrative roles include:

A. Communications Officer

- Create requests
- Submit content

B. Reviewer

- Review generated outputs
- Request revisions

C. Approver

- Approve or reject content

D. Operations Manager

- View dashboards
- Monitor workflows

E. Administrator

- Manage users
- Configure system settings

Permissions are enforced at both application and API layers.

Data Segregation

The platform supports:

A. Role-Based Segregation

Users access only authorized information.

B. Functional Segregation

Each business function operates within defined permissions.

C. Environment Segregation

Separate environments for:

- Development
- Testing
- Staging
- Production

D. Tenant/Department Segregation

Can be enabled if required by Dubai Police operational policies.

2.6 Cybersecurity Controls & Government Security Approach

The solution is designed following defense-in-depth principles.

A. Identity Security

- MFA
- SSO
- Role-Based Access Control
- Least Privilege Access

B. Network Security

- Private network segmentation
- Controlled ingress and egress
- Network security policies
- API access controls

C. Data Security

- Encryption in transit (TLS)
- Encryption at rest
- Secure key management
- Secrets management

D. Application Security

- Secure coding practices
- API authentication and authorization
- Input validation
- Audit logging
- Dependency vulnerability management

E. AI Security Controls

- Human-in-the-loop approvals
- Content Safety validation
- Prompt governance
- Output validation
- Full auditability of AI-generated content

F. Monitoring & Incident Detection

- Centralized logging
- Security event monitoring
- Audit trail retention
- Operational alerting
- Performance monitoring

G. Compliance Approach

The final compliance model will be aligned with Dubai Police security requirements, infrastructure standards, and applicable government policies during the detailed design phase.

The solution architecture is designed to support:

- Security-by-design principles
- Least-privilege access models
- Auditability and traceability
- Data protection controls
- Operational governance and oversight

3. AI Governance & Accuracy (Critical Requirement)

3.1 Methodology for Achieving and Measuring Target Accuracy (97%+)

The proposed solution adopts a human-governed AI operating model combining AI-assisted content generation, automated validation controls, and structured human review workflows.

Accuracy Framework

The platform will measure accuracy through a combination of:

- Automated quality evaluation
- Human reviewer validation
- Governance approval checkpoints
- Continuous feedback and model tuning

Multi-Layer Validation Approach

Layer 1 - AI Generation

AI-generated outputs are produced using approved Azure AI services and predefined prompt templates.

Layer 2 - Automated Validation

Generated content is evaluated against:

- Content completeness requirements
- Formatting standards
- Language quality rules
- Policy compliance checks
- Business-specific validation rules

Layer 3 - Human Review

Human reviewers validate:

- Factual correctness
- Communication suitability
- Context relevance
- Brand and policy alignment

Layer 4 - Approval Workflow

Content is only approved for publication after reviewer and approver validation.

Accuracy Measurement Approach

The proposed KPI framework may include:

Metric	Example Measurement
Content Acceptance Rate	% of AI outputs approved without major rework
First-Pass Approval Rate	% approved in first review cycle
Human Correction Rate	% of content requiring edits
Translation Accuracy Score	Human-reviewed translation quality

Metric	Example Measurement
Monitoring Classification Accuracy	Validated sentiment/topic classification accuracy
User Satisfaction Rating	Reviewer feedback scores

The overall accuracy target will be monitored through ongoing evaluation against approved benchmark datasets and operational review processes.

3.2 Hallucination Reduction & Source Referencing Controls

Recognizing that generative AI systems may produce inaccurate or unsupported outputs, the solution incorporates multiple controls to reduce hallucinations.

Controlled Prompting

Use of:

- Structured prompts
- Approved templates
- Defined output formats
- Agent-specific instructions

This reduces open-ended responses and improves consistency.

Context-Constrained Generation

Where applicable, agents are provided with:

- Approved communication guidelines
- Campaign briefs
- Historical approved content
- Policy documents

The model is instructed to rely on supplied context rather than assumptions.

3.3 Human Verification

All externally published content remains subject to human review and approval before release.

Source Attribution Support

For monitoring and intelligence use cases, the platform can retain references to:

- News articles
- Social media sources
- Monitoring feeds
- Internal documents

allowing reviewers to verify generated summaries against original sources.

Governance Rule

No AI-generated content is automatically published without review and approval.

Human-in-the-Loop Governance

The platform follows a human-in-the-loop operating model.

All high-impact outputs are reviewed before publication.

Typical workflow:

AI Generation >> Governance Validation >> Reviewer Assessment >> Approver Validation >> Publication

Sensitive Topic Handling

The solution supports configurable workflows for content involving:

- Public safety communications
- Crisis communications
- Legal or regulatory matters
- Reputation-sensitive topics
- High-visibility public messaging

Additional review stages can be enforced based on business rules and governance policies.

Content Safety Controls

The proposed architecture incorporates Azure AI Content Safety capabilities for screening:

- Harmful content
- Offensive content
- Unsafe instructions
- Policy violations

before content progresses through approval workflows.

Microsoft documents Azure AI Content Safety as a service for detecting potentially harmful user-generated and AI-generated content. This capability can be integrated into the content validation pipeline.

Bias Management Approach

The solution follows Microsoft Responsible AI principles and applies:

- Human oversight
- Review checkpoints
- Prompt governance
- Testing using representative scenarios
- Periodic output reviews

Bias detection and mitigation activities should be incorporated into operational governance processes throughout the solution lifecycle.

Microsoft's Responsible AI guidance emphasizes fairness, transparency, accountability, reliability, privacy, and human oversight as core principles for AI systems.

3.4 Prompt Management & Model Governance Framework

To ensure consistency, auditability, and controlled AI behaviour, the solution includes a structured Prompt Governance Framework.

Prompt Library

Approved prompts are maintained centrally and version controlled.

Examples:

- Press release generation prompts
- Campaign generation prompts
- Monitoring analysis prompts
- Translation prompts

Version Management

Prompt versions are tracked and managed similarly to application code.

Changes can be:

- Reviewed
- Approved
- Tested
- Audited

before deployment.

Role-Based Prompt Administration

Prompt modification privileges are restricted to authorized administrators.

Typical roles include:

- AI Administrator
- Solution Owner
- Governance Team
- Content Operations Team

Prompt Testing Process

Prior to release, prompt changes can be evaluated against:

- Approved test cases
- Historical content samples
- Quality benchmarks
- Governance requirements

Model Governance

The platform maintains visibility of:

- Model versions
- Model configurations
- Prompt versions
- Agent usage patterns
- Token consumption
- AI performance metrics

This supports traceability and operational governance.

Auditability

All significant AI activities may be logged, including:

- User request
- Agent invoked
- Prompt version used
- Model used
- Generated output
- Review decisions
- Approval actions

This creates a complete audit trail supporting governance and accountability requirements.

Proposed Governance Principles

The solution is designed around the following AI governance principles:

- Human Oversight
- Responsible AI
- Content Safety Validation
- Prompt Governance
- Controlled Publication
- Auditability & Traceability
- Role-Based Access Control
- Continuous Accuracy Monitoring
- Bias Awareness & Review
- Security-by-Design

4. Integrations

4.1 Required Integrations

The following integrations are considered essential for delivering the functional scope described in the RFQ.

Integration Area	Purpose	Proposed Approach
Identity & Authentication	User login and access management	Microsoft Entra ID/Corporate Identity Provider
File Storage & Asset Repository	Storage of documents, images, videos and generated assets	Azure Blob Storage or Dubai Police-approved repository
AI Services	Content generation, translation, vision and NLP capabilities	Azure OpenAI, Azure AI Vision, Azure AI Language
Email Notifications	Workflow approvals and alerts	SMTP/Corporate Mail Service
Audit Logging	Governance and traceability	Centralized audit repository
Dashboard & Reporting	Operational monitoring and governance visibility	Native platform dashboards and reporting services

4.2 Optional Integrations

The following integrations may provide additional value but are dependent on business requirements, licensing, and availability of external systems.

Media Libraries/Digital Asset Management (DAM)

Examples:

- Existing media repositories
- Digital asset management platforms
- Photo/video archives

Potential Use Cases:

- Retrieve approved assets
- Search historical campaigns
- Reuse approved media

Social Publishing Platforms

Examples:

- X (Twitter)
- Facebook
- Instagram
- LinkedIn
- YouTube

Potential Use Cases:

- Publish approved content
- Schedule posts
- Campaign distribution

Note:

Availability and functionality remain subject to platform APIs, permissions, and terms of service.

Workflow & Case Management Systems

Potential Use Cases:

- Escalation workflows
- Case management
- Approval routing

Examples may include:

- Microsoft Power Platform
- ServiceNow
- Internal workflow systems

Alerting Channels

Examples:

- Email
- SMS
- Microsoft Teams
- Internal notification platforms

Potential Use Cases:

- Approval notifications
- Monitoring alerts
- Escalation alerts

Internal Dubai Police Systems

Potential Use Cases:

- Content approval systems
- Records management
- Operational dashboards
- Internal communication platforms

Specific integrations will be confirmed during discovery and detailed design phases.

4.3 Third-Party Integrations

The following integrations of 3rd party are not considered in the proposal:

Category	Product/Service	Required	Licensing Model	Included in Proposed Solution
AI Services	Azure OpenAI	Yes	Consumption-based (Microsoft Azure)	No
AI Services	Azure AI Vision	Yes	Consumption-based (Microsoft Azure)	No
AI Services	Azure AI Language	Yes	Consumption-based (Microsoft Azure)	No
Cloud Infrastructure	Microsoft Azure Hosting Services	Yes (for cloud deployment option)	Consumption-based	No
Identity & Authentication	Microsoft Entra ID (if used)	Depends on customer environment	Customer Subscription	Customer Provided
Email Services	SMTP/Enterprise Mail Service	Yes	Customer-owned	Customer Provided
SMS Notifications (if required)	SMS Gateway Provider	Optional	Usage-based	Customer Provided
WhatsApp Notifications (if required)	WhatsApp Business Provider	Optional	Usage-based	Customer Provided
Social Media Publishing APIs	X, Facebook, Instagram, LinkedIn, YouTube APIs	Optional	Subject to platform terms and subscription requirements	Customer Provided

Category	Product/Service	Required	Licensing Model	Included in Proposed Solution
Social Listening Platforms	Brandwatch	Optional	Vendor Subscription	Customer Provided
Social Listening Platforms	Meltwater	Optional	Vendor Subscription	Customer Provided
Social Listening Platforms	Sprinklr	Optional	Vendor Subscription	Customer Provided
Social Listening Platforms	Talkwalker	Optional	Vendor Subscription	Customer Provided
Monitoring Data Sources	Commercial News/Media Monitoring Feeds	Optional	Vendor Subscription	Customer Provided
Map/Geolocation Services (if required)	Third-party mapping providers	Optional	Vendor Licensing	Customer Provided

Licensing Assumptions

Included within Solution Scope

The proposed application platform includes:

- React-based Web Portal
- Node.js Microservices
- Multi-Agent Orchestration Framework
- Approval Workflow Engine
- Governance Dashboard
- Audit & Reporting Components
- Integration Framework
- API Layer

Customer-Provided or Separately Billed Services

The following are assumed to be procured directly by Dubai Police or billed separately under cloud consumption:

Microsoft Azure Services

Including but not limited to:

- Azure OpenAI
- Azure AI Vision
- Azure AI Language

- Azure Storage
- Azure Database for PostgreSQL
- Azure Monitor
- Azure Kubernetes Service (AKS)

Charges are governed by Microsoft's published pricing and subscription terms.

Social Listening Platforms

If social listening capabilities are required beyond publicly available sources, licensing may be required for platforms such as:

- Brandwatch
- Meltwater
- Sprinklr
- Talkwalker

Selection will depend on business requirements and existing Dubai Police contracts.

Social Publishing Platforms

Publishing capabilities are subject to:

- Platform API availability
- Customer-owned social media accounts
- Applicable platform subscription requirements
- Vendor terms of service

5. Implementation Timeline

5.1 Detailed Implementation Timeline

Phase	Week	Key Activities	Key Milestones
Phase 1 Discovery & Planning	Week 1-4	Kick-off meeting and stakeholder interviews. Confirm scope, workflows, UI, and agent requirements. Map all integrations and data sources. Define approval rules, user roles, and escalation matrix. Identify security and data privacy requirements.	>> Project plan signed off. >> UI Design. >> Requirements register finalised. >> Workflow map approved. >> Integration list confirmed. >> Risk register baselined.
Phase 2 Configuration & Build	Week 5-18	UI Confirmation and Prototyping. Set up Azure environment (UAE North region). Configure all four AI agents with custom prompts, Arabic/English language rules, and brand guidelines. Build governance dashboard. Set up user roles and	>> All four agents configured and internally tested. >> Dashboard live in staging environment. >> Role matrix and permissions set up. >> Audit log running.

Phase	Week	Key Activities	Key Milestones
		permissions via Azure Active Directory. Configure audit logging and workflow stages. Connect approved integrations.	>> Draft workflows approved by Dubai Police.
Phase 3 Testing & Validation	Week 12-18	Run functional testing for all agents. Output quality testing against Dubai Police content standards. Security and access control testing. Workflow and approval flow testing. User Acceptance Testing (UAT) with Dubai Police team. Defect resolution and re-testing.	>> All agents pass functional testing. >> UAT completed and signed off. >> Security checks passed. >> Defect log cleared. >> Acceptance report submitted.
Phase 4 Training & Handover	Week 19-20	Conduct role-based training sessions for all user types (requesters, reviewers, approvers, administrators). Deliver user manuals and admin guide. Hand over prompt configuration documents and workflow documentation. Provide recorded training sessions for future onboarding. Final handover pack submitted.	>> All user groups trained. >> User manuals and admin guide delivered. >> Prompt and configuration docs handed over. >> Handover pack accepted.
Phase 5 Go-Live & Support	Week 21-23 + Ongoing	Deploy approved platform to production environment. Monitor performance and agent output quality. Fine-tune workflows and prompts based on real usage. Provide hypercare support for first 4 weeks post go-live. Transition to standard SLA-based support. Begin hybrid/on-premise migration planning if required.	>> Platform live in production. >> Go-live report submitted. >> SLA support model activated. >> Optimisation log maintained. >> Migration roadmap agreed (if applicable).

5.2 Key Milestones

Summary View

Phase	Duration
Phase 1 - Discovery & Planning	Week 1-3
Phase 2 - Configuration & Build	Week 4-10
Phase 3 - Testing & Validation	Week 11-14
Phase 4 - Training & Handover	Week 15-17
Phase 5 - Go-Live & Support	Week 18-20 + Ongoing

5.3 Dependencies Required from Dubai Police

Access & System Setup

- Assign a project owner and main point of contact from Dubai Police
- Provide Azure Active Directory (Entra ID) access or SSO configuration details
- Ensure all users have system access before training begins
- Confirm production environment access and deployment approvals
- Assign an internal system administrator for post go-live

Content & Brand Materials

- Brand guidelines, approved templates, logos, fonts, and tone-of-voice documents
- Historical Arabic and English press releases and campaign samples
- Approved keywords, prohibited wording, and terminology glossary
- Sample briefs, press releases, and campaign examples for agent training

Technical Specifications

- Digital screen specifications (screen ID, size, orientation, aspect ratio, safe zones)
- IT and cybersecurity requirements and compliance standards
- Confirm on-premise migration readiness (hardware, network, security) — if applicable

Workflows & Rules

- User role list and approval hierarchy
- Escalation matrix and publishing rules
- Monitoring topics, trusted sources, and fraud/risk indicators for Agent 4
- Test cases for monitoring and misinformation detection

Testing & Training

- Assign 2-3 users from media team, IT team, and approver level for UAT
- Review and provide feedback on agent outputs during UAT
- Confirm acceptance criteria before testing begins
- Arrange and confirm training sessions with relevant teams
- Provide feedback on training materials before finalisation

5.4 Resource Requirement

5.4.1 Team Structure - Vendor

Role	Responsibility
Project Manager	Project governance, planning, stakeholder management
Business Analyst	Requirements gathering, process mapping, user stories, UAT coordination
Solution Architect	Solution architecture, AI architecture, security, integration strategy
UI/UX Designer	Wireframes, prototypes, dashboard and portal design
Frontend Developers (React)	Dashboard, portal UI, workflow screens
Backend Developers (Node.js/NestJS)	Microservices, APIs, integrations, workflow engine
AI/ML Engineers	Agent development, prompt engineering, Azure AI integration, LangGraph workflows
Database Engineer	PostgreSQL design, optimization, data governance
QA/Test Engineers	Functional, integration, automation and UAT support
DevOps Engineer	Azure infrastructure, CI/CD pipelines, deployment automation
Security Engineer (Part-Time)	Security review, RBAC validation, hardening, compliance support

5.4.2 Team Structure from Dubai Police

Team	Involvement during	Responsibility
Business Team	Discovery and UAT phases	• Project Sponsor • Product Owner/Business Lead • Communications Representatives • Governance Representatives
IT & Security Team	Design, Integration, and Deployment Activities	• Infrastructure Representative • Security Representative • Identity Management Representative
UAT Team	UAT execution	• Reviewers • Approvers • Operational Users

6. Training, Documentation, Support & SLA

6.1 Training & Knowledge Transfer Approach

We believe that successful adoption of the Dubai Police Agentic AI Media Operations Platform depends on effective knowledge transfer, structured training, and operational readiness. The training program is designed to ensure all stakeholders can confidently utilize, administer, govern, and support the platform.

Training Areas

Training Area	Target Audience	Coverage
User Training	Communications Officers, Content Creators	Request creation, content generation, campaign management, screen adaptation requests, monitoring requests, dashboard usage
Reviewer Training	Reviewers, Governance Teams	Content review process, validation workflows, revision requests, approval recommendations
Approver Training	Approvers, Management Users	Approval workflows, governance controls, escalation handling, audit review
Administrator Training	System Administrators	User management, role configuration, workflow configuration, prompt management, platform administration
Technical Training	IT & Support Teams	Architecture overview, integrations, deployment model, monitoring, troubleshooting, maintenance
Governance & AI Operations Training	Governance Teams	Prompt governance, AI controls, audit management, content safety, compliance monitoring

6.2 Training Deliverables

Key Components of Training Program

1. Interactive Workshops

Hands-on training sessions covering platform workflows, AI agent operations, governance controls, and approval processes.

2. Feature Walkthroughs

Detailed demonstrations of:

- Media Release Agent
- Campaign Creative Agent
- Screen Adaptation Agent
- Monitoring Intelligence Agent
- Governance Dashboard

3. Technical Training

Technical enablement sessions for administrators and IT teams covering:

- System architecture
- Security controls
- User administration
- Monitoring and troubleshooting
- Configuration management

4. Platform Administration Training

Training on:

- User and role management
- Workflow configuration
- Prompt management
- Knowledge base administration
- Audit management

5. Governance & Compliance Training

Training on:

- Human-in-the-loop workflows
- Approval controls
- Audit requirements
- AI governance policies
- Content safety procedures

6. Best Practices & Operational Guidance

Guidance on:

- Effective prompt usage
- Content quality management
- Governance procedures
- Operational monitoring
- Continuous improvement practices

6.3 Documentation Deliverables

The following documentation will be provided as part of the implementation and handover process.

Document	Description
User Manual	End-user guide covering request creation, content generation, reviews, approvals, monitoring, and reporting
Reviewer Guide	Review workflows, validation procedures, revision handling, governance checks
Approver Guide	Approval process, escalation management, governance responsibilities
Administrator Guide	User management, role configuration, workflow administration, system settings
Technical Architecture Document	Solution architecture, infrastructure components, integrations, security architecture
API & Integration Documentation	Integration architecture, endpoints, authentication methods, data flow specifications
Prompt Governance Guide	Prompt management process, versioning controls, testing procedures, approval workflows
Deployment & Operations Guide	Deployment procedures, environment configuration, monitoring, backup and recovery
Support Runbook	Operational support procedures, troubleshooting guides, escalation process
Knowledge Transfer Materials	Training presentations, recorded sessions, FAQs, reference materials

6.4 Knowledge Transfer & Handover

The project includes structured knowledge transfer activities to ensure operational independence following deployment.

Handover Activities

Activity	Description
Functional Knowledge Transfer	Platform workflows, agent operations, approval processes
Administrative Knowledge Transfer	Configuration management, user administration, governance controls
Technical Knowledge Transfer	Architecture, integrations, deployment model, monitoring and support procedures
Documentation Handover	Delivery of all approved project documentation
Recorded Training Sessions	Training recordings for future onboarding and reference
Operational Readiness Review	Final validation of support readiness and ownership transfer

6.5 Post Go-Live Support Model

Following production deployment, the project includes a structured hypercare and support phase to ensure platform stability and user adoption.

Hypercare Support

Support Activity	Description
Go-Live Support	Production deployment assistance and validation
User Support	User onboarding assistance and issue resolution
Defect Management	Production defect triage and prioritization
Workflow Optimization	Minor workflow and configuration adjustments
Prompt Tuning Support	Prompt refinements based on operational feedback
Performance Monitoring	Monitoring platform health and operational metrics

Ongoing Support Services

Service	Description
Incident Management	Investigation and resolution of reported issues
Platform Monitoring	Monitoring system availability and performance
Security Updates	Security patches and vulnerability remediation
Maintenance Releases	Bug fixes and platform improvements
Configuration Support	Workflow, user, and platform configuration assistance
Technical Assistance	Support for operational and administrative teams

6.6 Proposed SLA Framework

Incident Response Targets

Priority	Description	Response Time	Resolution Target
P1 - Critical	Complete system outage or business-critical functionality unavailable	1 Hour	4 Hours (Workaround)/1 Business Day
P2 - High	Major functionality impacted with no acceptable workaround	4 Hours	2 Business Days
P3 - Medium	Partial functionality issue with workaround available	8 Business Hours	5 Business Days
P4 - Low	Minor issue, enhancement request, cosmetic issue	1 Business Day	Planned Release Cycle

Service Availability

Service Metric	Target
Platform Availability	99.5% Monthly Uptime
Support Availability	Business Hours Support (UAE Working Hours)
Monitoring Coverage	24x7 Infrastructure Monitoring
Incident Escalation	Multi-Level Escalation Process
Planned Maintenance	Scheduled with Prior Notification

6.7 Other Information

Item	Description
Go-Live	Production deployment following successful UAT and acceptance sign-off
Source Code Handover	Source code, deployment artifacts, and technical documentation can be provided as per agreed commercial and contractual terms
Hypercare Support	4 weeks post-go-live support included for stabilization and operational assistance
Maintenance	Ongoing support and AMC services can be provided under a separate support agreement
Third-Party Services	Azure services, AI services, social listening tools, and external APIs are customer-provided unless explicitly included
Integrations	Limited to approved scope and confirmed during discovery and design phases
Documentation	Comprehensive functional, administrative, technical, and operational documentation included
User Training	Role-based training sessions for users, reviewers, approvers, administrators, and IT teams
Knowledge Transfer	Structured handover sessions, operational readiness review, and training recordings included

7. Commercial Proposal - Agentic AI Media Operations Platform Dubai Police

7.1 One-Time Implementation Cost

Component	Description	Estimated Cost (AED)
Agent 1 - Media Release Agent	Setup, prompt engineering, Arabic/English configuration, workflow build, testing	
Agent 2 - Campaign Creative Agent	Setup, campaign brief processing, visual concept generation, multilingual config	
Agent 3 - Screen Adaptation Agent	Screen spec mapping, visual fit analysis, bulk adaptation engine, preview sheet generation	
Agent 4 - Monitoring Intelligence Agent	Source configuration, topic tracking, sentiment setup, escalation matrix, alert routing	
Governance Dashboard	Role-based dashboard, audit log, approval workflows, metrics, reporting views	
Platform Setup & Integration	Azure environment setup, SSO/Entra ID integration, security configuration, deployment	

Component	Description	Estimated Cost (AED)
Project Management & BA	Discovery, planning, documentation, stakeholder coordination across all phases	
Total One-Time Cost		

7.2 Hosting & Infrastructure (Annual)

Service	Dev	Stage	Prod	Total AED/Year
AKS + Compute Nodes				
Azure Container Registry				
PostgreSQL Flexible Server				
Blob Storage				
Key Vault				
Application Gateway WAF				
Azure Monitor & Log Analytics				
Networking (Public IP, NAT, Traffic)				
Azure DevOps (Repos, Pipelines, Artifacts)				
Azure OpenAI				
Azure AI Vision				
Azure AI Language				
Azure AI Content Safety				

Note: he above costs are rough-order-of-magnitude estimates prepared for budgeting purposes only and are based on a three-environment deployment model (Development, Staging, and Production) hosted in Microsoft Azure UAE North. Actual costs will vary depending on selected SKUs, Azure service consumption, AI transaction volumes, storage growth, monitoring retention policies, and final infrastructure sizing determined during the Discovery & Planning phase.

7.3 Support & SLA Fees (Annual)

Support Tier	Coverage	Estimated Cost (AED/Year)
Hypercare Support (First 4 weeks post go-live)	Dedicated support, daily check-ins, fast issue resolution	Included in implementation
Standard SLA Support	Bug fixes, prompt tuning, configuration updates, user support, monthly reporting	
SLA Response Times	Critical: 4 hours/High: 8 hours/Medium: 24 hours/Low: 72 hours	Included in SLA
Quarterly Platform Reviews	Performance review, optimization, model updates, usage analysis	Included in SLA
Total Annual Support		

7.4 Third-Party Licenses & Tools

Tool/Service	Purpose	Estimated Cost (AED/Year)
Social Listening Tool (e.g. Brandwatch/Mention)	External source monitoring for Agent 4	
Social Publishing Tool (e.g. Hootsuite/Sprinklr)	Optional publishing workflow integration	
Stock Image/Asset Library (if required)	Licensed visual assets for campaign generation	
Data Provider/News Feed API	Real-time news and public data feed for monitoring	
Total Third-Party (Estimated Range)		

Note: Third-party tools are optional based on Dubai Police's existing subscriptions. If Dubai Police already holds licenses for any of the above tools, integration cost only will apply.

Key Notes

- All costs are exclusive of VAT (5%).
- One-time costs cover design, build, testing, training, and handover across all 5 phases.
- Dashboard and governance layer cost is **included** in the one-time implementation cost.
- Recurring costs begin from go-live date, not contract signing date.

- Sora video generation is listed separately as it remains consumption-based and subject to Azure availability in the UAE region.
- Final costs will be confirmed after the discovery phase based on actual scope, usage volumes, and integration complexity.

8. Risks, Exclusions & Optional Enhancements

8.1 Key risks, their impact, and approach for mitigation.

Risk	Impact	Mitigation Approach
Delayed stakeholder feedback, approvals, or requirements sign-off	May impact sprint timelines and project schedule	Establish governance structure, defined review cycles, and nominated business representatives with decision-making authority
Delayed access to Dubai Police systems, environments, APIs, or infrastructure	May delay integrations, testing, and deployment activities	Confirm access requirements during discovery phase and track dependencies through project governance meetings
Incomplete or evolving business requirements	May result in rework, scope changes, or schedule impacts	Conduct detailed discovery workshops, backlog prioritization, and formal change management process
Availability and quality of source content, historical data, or media assets	May impact AI output quality, testing, and validation activities	Define data requirements early and validate sample datasets during discovery and design phases
Third-party API limitations, rate limits, or licensing restrictions	May affect integration capabilities or performance	Perform integration assessment during discovery and align implementation with supported vendor capabilities
Changes in third-party platforms, APIs, or licensing models	May require integration updates or additional effort	Design integrations using abstraction layers and monitor vendor roadmap and API changes
AI-generated content requiring additional human review or revisions	May increase review cycles and operational effort	Implement governance controls, prompt management, approval workflows, and human-in-the-loop validation processes
Security, compliance, or infrastructure approval delays	May affect deployment readiness and go-live timelines	Engage IT and security stakeholders early and conduct periodic architecture and security reviews
Cloud service consumption exceeding estimated volumes	May increase operational costs	Implement monitoring, usage controls, dashboards, and cost governance processes

Risk	Impact	Mitigation Approach
Dependency on external vendors for social listening, publishing, or data sources	May impact delivery schedules if vendor onboarding is delayed	Identify required third-party services early and align onboarding activities with project milestones

8.2 Exclusions

- Data Migration
- Third-Party Software Licenses
- Third-Party Product Procurement
- Infrastructure Procurement
- Enterprise-Wide Change Management
- Custom Integrations Not Identified During Discovery
- Production Support Beyond Agreed Hypercare Period
- AI Model Training or Fine-Tuning
- External Security Certifications and Audits
- Multi-Language Expansion Beyond Agreed Scope
